

ACTIVE - ROAD GATED REQUIRES KEY



BC Ministry of
Forests and Range

Page 1 of 2

Corporate Bridge Register (CBR) Structure Inventory Data Form "BRIDGES"

GENERAL	
*Structure #	*Site #: CK-2068
*Type/Class: ☒ Permanent Bridge ☐ Temporary Bridge	Crossing Name:
*Forest District: Chilliwack	Management Area:
*Forest Service Road: SLESSE CRK	Kilometres: 6.1
*Project File ID#: 5127	*Br. 07
Built For: ☐ BC Timber Sales ☐ Operations Division ☐ Other Commercial Users ☐ Road Permit Holder ☐ Road Use Permit Holder	
*Source: ☐ Inherited: Found Structure ☐ Inherited: From Oil & Gas/ ☐ Inherited: Non-Status Road ☐ Other Ministry ☐ Inherited: Reallocation ☐ Inherited: Transfers from ☐ New Structure ☐ Other Ministries ☐ Replacement Structure	
Year Built:	Year Added to Inventory:
Current Load Rating GVW (tonnes): <small>(PEng to enter / update this value on structure details screen in CBR)</small>	Design Load Rating GVW (tonnes): <small>(Typically obtained from design drawings)</small>
Design Vehicle Configuration: ☐ BCL625 ☐ CL625 ☐ L100 ☐ L120 ☐ L150 ☐ L165 ☐ L45 ☐ L60 ☐ L75 ☐ L90 ☐ Other	
*Primary User Client Number:	*Client Location Code:
Primary User Name:	
As Built Information on File? ☐ Yes ☐ No	
Installation Cost (\$):	Material Cost (\$):
REPLACEMENT DETAILS	
Original Replacement (year):	Estimated Closure (year):
Light Vehicle Traffic Replacement (year):	*Full Log Haul Traffic Replacement (year): <small>(PEng to review and evaluate inspector's estimate, and to enter /update this value on structure details screen in CBR).</small>
Estimated Replacement Cost (\$):	
Replacement Cost Comments:	

* Denotes Mandatory Information for Corporate Bridge Register



BC Ministry of
Forests and Range

Page 2 of 2

Corporate Bridge Register (CBR) Structure Inventory Data Form "BRIDGES"

CIC-2068

STRUCTURAL DETAILS

Number of Spans: 1	Length of Spans (m) [e.g. for a 3-span bridge – 20, 35, 20] 26.8 - 6	
Number of Piers: —	Pier Type: ☐ Concrete ☐ Crib - Timber ☐ Piles - Concrete ☐ Piles - Steel ☐ Piles - Timber Treated ☐ Piles - Timber Untreated ☐ Steel Column on Concrete Pad	
Needle Beams? ☐ Yes ☒ No	Portable Structure? ☐ Yes ☒ No	Portable Superstructure Status: ☐ Installed ☐ Storage

Portable Superstructure Storage Location:

*Bridge Length (metres): 27.4	*Superstructure: ☐ Compo Girders ☐ Concrete Box Beam ☐ Rail Car ☐ Concrete Cast in Place ☐ Concrete I/T Beam ☐ Other ☐ Concrete Slab Girders ☐ Glulam Girder ☐ Log Stringer ☐ Steel Box Beam ☒ Steel I-Beam ☐ Steel Truss/Bailey/Acrow ☐ Timber-Treated Stringers ☐ Timber-Untreated Stringers		
----------------------------------	---	--	--

*Deck Type: ☐ Concrete ☐ Concrete Composite ☐ Gravel ☐ Concrete Removable ☐ Concrete - Steel Free ☐ Steel ☐ Timber-Treated ☐ Timber-Untreated ☐ Other ☐ Timber-Treated Panels ☒ Timber-Untreated Panels	*Deck Width (metres): 3.9
---	------------------------------


*Running Surface: ☐ Anti-Skid ☐ Asphalt ☐ Concrete ☐ Gravel ☐ Not Available ☒ Timber Planks			
--	--	--	--

*Left Abutment: ☐ Binwall ☐ Concrete Cast in Place ☐ Concrete Lock Blocks ☐ Concrete Precast ☒ Crib, Log or Untreated Timber ☐ Other ☐ Pile-Temporary Materials ☐ Pile-Permanent Materials ☐ Sill-Permanent Materials ☐ Sill-Temporary Materials ☐ Steel Pipe & Precast Pad	*Right Abutment: ☐ Binwall ☐ Concrete Cast in Place ☐ Concrete Lock Blocks ☐ Concrete Precast ☒ Crib, Log or Untreated Timber ☐ Other ☐ Pile-Temporary Materials ☐ Pile-Permanent Materials ☐ Sill-Permanent Materials ☐ Sill-Temporary Materials ☐ Steel Pipe & Precast Pad
--	---

Comments:

**Routine Condition Bridge Inspection Form**
(except for log stringer or timber stringer bridges)

GENERAL INFORMATION				(enter either long/lat or UTM below - not both)			
*Site #: <u>CK-2068</u>	*Crossing Name:	*Type/Class: ☐ Temporary bridge ☒ Permanent bridge	*Project File ID# <u>5127</u>				
*Structure #:			*Br. <u>07</u>				
*FSR Name: <u>SLESSE CRK</u>	*Forest District: <u>Chilliwack</u>	*Kilometres: <u>6.1</u>	User km:				
Longitude: (ddd / mm / ss.s) <u>49 02 18.3</u>	☒ OR ☐	UTM Zone	UTM Easting	UTM Northing			
Latitude: (ddd / mm / ss.s) <u>121 39 48.2</u>							
LEFT/RIGHT APPROACHES (as seen facing downstream) E = excellent; G = good; F = fair; P = poor; N/A = not appl., UR = Unrated							
Item	Present Condition (circle or fill-in)	Comments (a comment is mandatory if condition "Poor" is selected)					
Alignment	E (G) F P UR						
Bridge Ahead Signs Missing	(0) 1 2						
Brushing Required	Yes (No)						
Delineator Missing Left	(0) 1 2						
Delineator Missing Right	(0) 1 2						
Fender Condition	E G F (P) None UR	NO FENDERS ON LEFT APPROACH.					
Posted Load Rating	(tonnes) or None	NOT POSTED.					
Road Surface	E (G) F P UR						
LEFT/RIGHT ABUTMENTS (as seen facing downstream)							
Item	Present Condition (circle)	Comments (a comment is mandatory if condition "Poor" is selected)					
Log/Timber Cribs	E G (F) P N/A UR	5x CRIB ON LEFT ABUT, 1x ON RIGHT. CLOSED FACED.					
Tie-backs	E G (F) P N/A UR	3x, ONE OF THE TIEBACKS ROTTEN & NOW BROKEN. ~ 10-20cm off S&P ROT.					
Bin Wall	E G F P (N/A) UR						
Concrete (cast in place; lock blocks, precast)	E G F P (N/A) UR						
Caps or Sills	E G F P (N/A) UR						
Piles or Posts	E G F P (N/A) UR						
Ballast Wall	E G (P) P N/A UR	TIMBER.					
Wing Wall	E G F P (N/A) UR						
Bracing	E G F P (N/A) UR						
Hardware	E G (F) P N/A UR	LASHED.					
Fill	E G (F) P N/A UR						
Riprap	E (G) F P N/A UR	WELL RIPRAPED UPSTREAM ALONG CHANNEL.					
Bearings	E G (F) P N/A UR						
Corrosion Protection	E G F P (N/A) UR						
Span 1 of 1 (spans are numbered consecutively starting from the left abutment) Use "Additional Spans" Sheet for Multiple Spans							
DECK							
Item	Present Condition (circle)	Comments (a comment is mandatory if condition "Poor" is selected)					
Running Surface (N/A if running surface is gravel or timber planks)	E G F P (N/A) UR						
Running Planks	(E) G F P N/A UR	4" x 10 - TREATED TIMBER					
Sub-deck	(E) G F P N/A UR	4" x 10 TREATED TIMBER					
Ties	(E) G F P N/A UR	200 x 250mm - TREATED TIMBER					
Nails	(E) G F P N/A UR						
Deck to Girder Bolts	E G F P (N/A) UR						
Concrete Deck	E G F P (N/A) UR						
Grout Pockets	E G F P (N/A) UR						
Deck Joints	E G F P (N/A) UR						
Steel Deck Plate	E G F P (N/A) UR						
Gravel Surface	E G F P (N/A) UR						
Gravel Deck Depth	metres or N/A						
Curb Rail/Blocks/Posts	(E) G F P UR	NEW TIMBER - TREATED					
Handrails/Walkouts	(E) G F P N/A UR	" " " "					
Hardware	(E) G F P N/A UR						
Overall Deck Condition	E (G) F P UR						


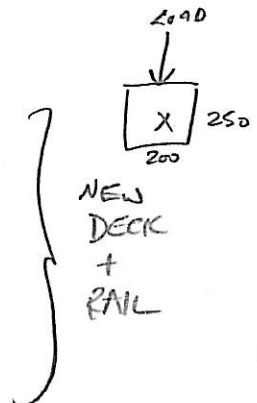


**Routine Condition Bridge Inspection Form**
(except for log stringer or timber stringer bridges)

GENERAL INFORMATION			
*Site #: CK-2068		*Structure #:	
SUPERSTRUCTURE			
Item	Present Condition (circle)	Comments (a comment is mandatory if condition 'Poor' is selected)	
Girders	E (G) F P UR		
Diaphragms	E G F P (N/A) UR		
Bracing	E (G) F P N/A UR		
Under-trussing	E G F P (N/A) UR		
Hardware	E (G) F P N/A UR		
Welded / Grouted Shear Connectors	E G F P N/A UR		
Stream CHANNEL			
*Est. Present Water Level Depth 0.5 (m)		*Est. Present Water Level Depth 1.2 (m)	*Est. Present Water Level Depth 2 (m)
HAZARDS (circle yes or no for each item)			
High Water?	Yes (No)	Scour?	Yes (No)
Ice?	Yes (No)	Debris?	Yes (No)
Aggradation?	Yes (No)		
Comments			
REPAIRS: ☐ Recommended ☐ Not required (H = High, M = Medium, L = Low)			
Repair Item #	*Priority (circle)	*Estimate (\$)	*Repair Description
1	(H) M L		LOAD LIMIT SIGN
2	(H) M L		FENDERS ON LEFT APPROACH
3	H M L		
*Monitoring Status: ☐ Recommended ☐ Not required			
Monitor Item #	*Monitor Description		
1			
2			
PHOTO LOG			
Photo #	Description	Photo #	Description
	LEFT TO RIGHT		RIGHT ABUT
	RIGHT TO LEFT		UNDERNEATH
	FROM UPSIDE		FROM DOWN STREAM
	LEFT ABUT		ROCKED TIEBACK
INSPECTOR TO COMPLETE THIS SECTION			
As-built Drawings Checked? Yes (No)		P Eng Inspection Required? Yes (No)	
		Inspector's Estimate of Full Log Haul Traffic Replacement Date (year): (P Eng to review and evaluate inspector's estimate, and to update "Full Log Haul Traffic Replacement (year)" on structure details screen in CBR)	
*Date of Inspection (yyyy/mm/dd) 2010-09-02	*Inspection Company Name Onsite Engineering Ltd	*Inspector's Name (print) Ali Sadeghi	Inspector's Signature
Inspector's Comments			
PROFESSIONAL ENGINEER (P Eng) TO COMPLETE THIS SECTION			
Current Load Rating GVW (tonnes): 54 (P Eng to update structure details screen in CBR as necessary)		Date of Next Planned Inspection (yyyy/mm/dd) 2012/09/01	
Reviewer Company Name Onsite Engineering LTD	Reviewed by - P Eng's Name (print) G. Dohm	Reviewed by - P Eng's Sign: 	Date Reviewed (yyyy/mm/dd) 2010/11/17
P Eng Reviewer's Comments L60 or 54 tonne load rating. Please post.			


* Denotes Mandatory Information for Corporate Bridge Register

ROTATION BALAST WALL

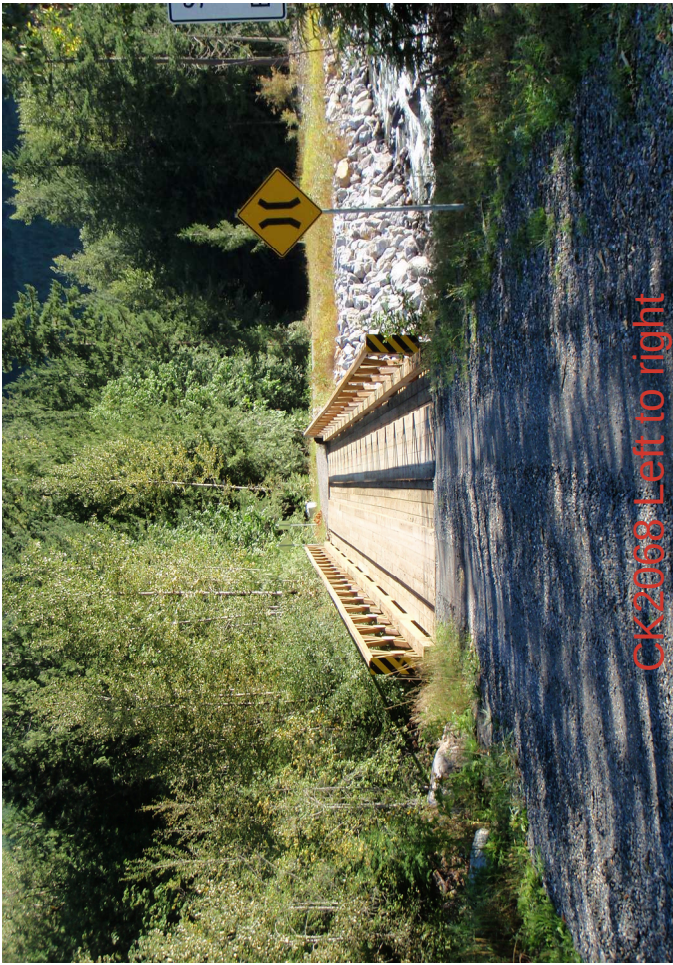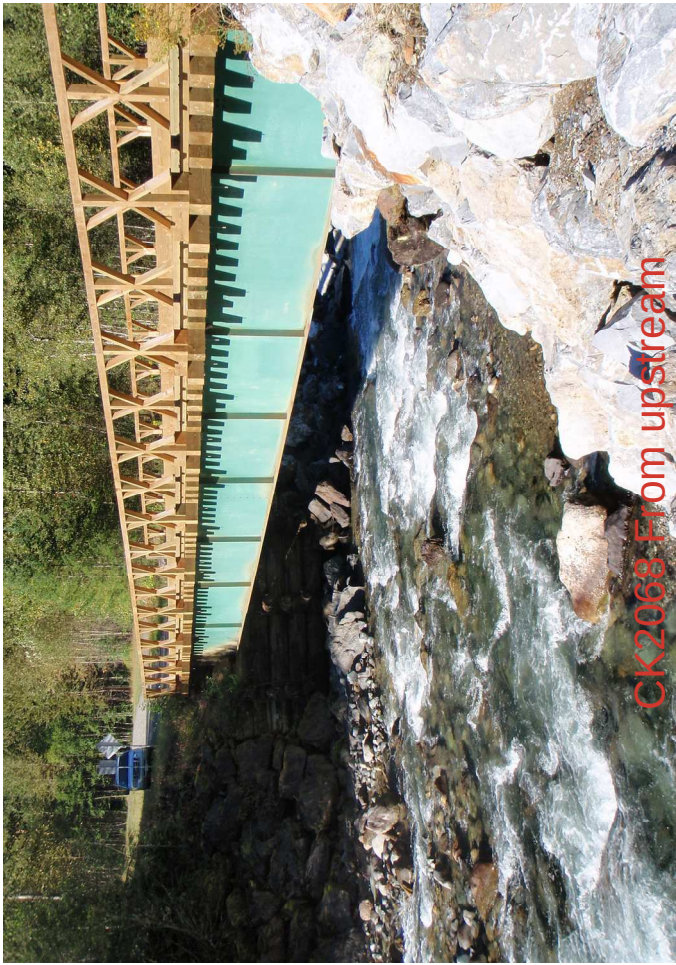



CK2068 Left abutment

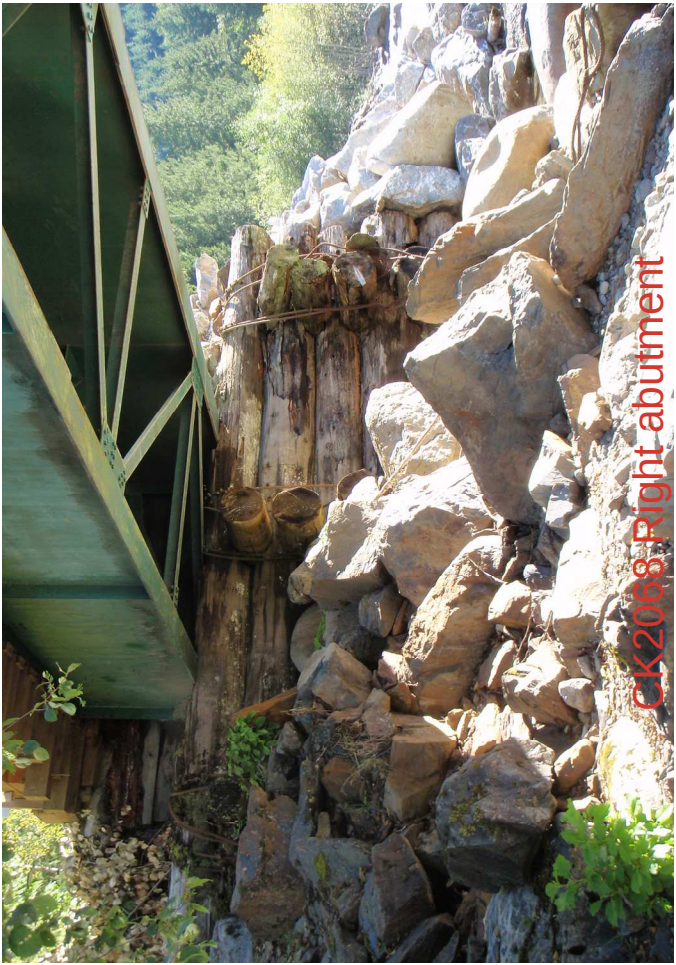

CK2068 Right abutment



CK2068 Underneath



CK2068 Fram downstream



CK2068 Right abutment rotten tie backs



CK2068 rotten balast wall
