

Aug 16

 BC Ministry of Forests and Range	Page 1 of 2
	Corporate Bridge Register (CBR) Structure Inventory Data Form "BRIDGES"

GENERAL	
*Structure #	*Site #: CK-2214
*Type/Class: ☐ Permanent Bridge ☐ Temporary Bridge	Crossing Name:
*Forest District: Chilliwack	Management Area:
*Forest Service Road: PEERS CK	Kilometres: 0.5
*Project File ID#: 8126	*Br. 01
Built For: ☒ BC Timber Sales ☐ Operations Division ☐ Other Commercial Users ☐ Road Permit Holder ☐ Road Use Permit Holder	
*Source: ☐ Inherited: Found Structure ☐ Inherited: From Oil & Gas/ ☐ Inherited: Non-Status Road Other Ministry ☐ Inherited: Reallocation ☐ Inherited: Transfers from ☐ New Structure Other Ministries ☐ Replacement Structure	
Year Built:	Year Added to Inventory:
Current Load Rating GVW (tonnes): (PEng to enter / update this value on structure details screen in CBR)	Design Load Rating GVW (tonnes): (Typically obtained from design drawings)
Design Vehicle Configuration: ☐ BCL625 ☐ CL625 ☐ L100 ☐ L120 ☐ L150 ☐ L165 ☐ L45 ☐ L60 ☐ L75 ☐ L90 ☐ Other	
*Primary User Client Number:	*Client Location Code:
Primary User Name:	
As Built Information on File? ☐ Yes ☐ No	
Installation Cost (\$):	Material Cost (\$):
REPLACEMENT DETAILS	
Original Replacement (year):	Estimated Closure (year):
Light Vehicle Traffic Replacement (year):	*Full Log Haul Traffic Replacement (year): (PEng to review and evaluate inspector's estimate, and to enter / update this value on structure details screen in CBR).
Estimated Replacement Cost (\$):	
Replacement Cost Comments:	

* Denotes Mandatory Information for Corporate Bridge Register

CK 2214

BC Ministry of
Forests and Range


Page 2 of 2

Corporate Bridge Register (CBR) Structure Inventory Data Form "BRIDGES"

STRUCTURAL DETAILS			
Number of Spans: 1		Length of Spans (m) [e.g. for a 3-span bridge – 20, 35, 20] 18.6	
Number of Piers: _____		Pier Type: ☐ Concrete ☐ Crib - Timber ☐ Piles - Concrete ☐ Piles - Steel ☐ Piles - Timber Treated ☐ Piles - Timber Untreated ☐ Steel Column on Concrete Pad	
Needle Beams? ☐ Yes ☒ No		Portable Structure? ☐ Yes ☒ No	Portable Superstructure Status: ☐ Installed ☐ Storage
Portable Superstructure Storage Location:			
*Bridge Length (metres): 12.5 19.2	*Superstructure: ☐ Compo Girders ☐ Concrete Box Beam ☐ Rail Car ☐ Concrete Cast in Place ☐ Concrete I/T Beam ☐ Other ☐ Concrete Slab Girders ☐ Glulam Girder ☐ Log Stringer ☐ Steel Box Beam ☒ Steel I-Beam ☐ Steel Truss/Bailey/Acrow ☐ Timber-Treated Stringers ☐ Timber-Untreated Stringers		
*Deck Type: ☐ Concrete ☐ Concrete Composite ☐ Gravel ☐ Concrete Removable ☐ Concrete - Steel Free ☐ Steel ☐ Timber-Treated ☐ Timber-Untreated ☐ Other ☒ Timber-Treated Panels ☐ Timber-Untreated Panels			*Deck Width (metres): 3.9
*Running Surface: ☐ Anti-Skid ☐ Asphalt ☐ Concrete ☐ Gravel ☐ Not Available ☒ Timber Planks			
*Left Abutment: ☐ Binwall ☐ Concrete Cast in Place ☐ Concrete Lock Blocks ☐ Concrete Precast ☐ Crib, Log or Untreated Timber ☐ Other ☐ Pile-Temporary Materials ☐ Pile-Permanent Materials ☐ Sill-Permanent Materials ☐ Sill-Temporary Materials ☒ Steel Pipe & Precast Pad		*Right Abutment: ☐ Binwall ☐ Concrete Cast in Place ☐ Concrete Lock Blocks ☐ Concrete Precast ☐ Crib, Log or Untreated Timber ☐ Other ☐ Pile-Temporary Materials ☐ Pile-Permanent Materials ☐ Sill-Permanent Materials ☐ Sill-Temporary Materials ☒ Steel Pipe & Precast Pad	
Comments:			

**Routine Condition Bridge Inspection Form**
(except for log stringer or timber stringer bridges)

GENERAL INFORMATION				(enter either long/lat or UTM below – not both)		
*Site #: <u>CK-2214</u>	*Crossing Name:	*Type/Class: ☐ Temporary bridge ☒ Permanent bridge	*Project File ID# <u>0126</u>			
*Structure #:			*Br. <u>01</u>			
*FSR Name: <u>PEEPS CK</u>	*Forest District: <u>Chilliwack</u>	*Kilometres: <u>0.3</u>	User km: <u>0.3</u>			
Longitude: (ddd / mm / ss.s) <u>49 23 03.0</u>	☒ OR	UTM Zone	UTM Easting	UTM Northing		
Latitude: (ddd / mm / ss.s) <u>121 19 00.7</u>						
LEFT/RIGHT APPROACHES (as seen facing downstream) E = excellent; G = good; F = fair; P = poor; N/A = not appl.; UR = Unrated						
Item	Present Condition (circle or fill-in)	Comments (a comment is mandatory if condition "Poor" is selected)				
Alignment	E G <u>(F)</u> P UR					
Bridge Ahead Signs Missing	0 <u>(1)</u> 2					
Brushing Required	<u>(Yes)</u> No	<u>MINOR</u>				
Delinicator Missing Left	<u>(0)</u> 1 2					
Delinicator Missing Right	<u>(0)</u> 1 2					
Fender Condition	E <u>(G)</u> F P None UR	<u>LOGS</u>				
Posted Load Rating	<u>54</u> (tonnes) or None					
Road Surface	E G <u>(F)</u> P UR	<u>POTHOLES ON APPROACHES</u>				
LEFT/RIGHT ABUTMENTS (as seen facing downstream)						
Item	Present Condition (circle)	Comments (a comment is mandatory if condition "Poor" is selected)				
Log/Timber Cribbs	E G F P <u>(N/A)</u> UR					
Tie-backs	E G F P <u>(N/A)</u> UR					
Blk Wall	E G F P <u>(N/A)</u> UR					
Concrete (cast in place; lock blocks, precast)	E G F P <u>(N/A)</u> UR					
Caps or Sills	E G F P <u>(N/A)</u> UR					
Piles or Posts	E G <u>(F)</u> P N/A UR	<u>PIPE PILES & N SPREAD FOOTINGS</u>				
Ballast Wall	E <u>(F)</u> P N/A UR	<u>PRECAST CONCRETE</u>				
Wing Wall	E <u>(F)</u> P N/A UR	<u>PRECAST CONCRETE</u>				
Bracing	E G <u>(F)</u> P N/A UR					
Hardware	E G <u>(F)</u> P N/A UR					
Fill	E <u>(G)</u> F P N/A UR					
Riprap	E G <u>(F)</u> P N/A UR					
Bearings	E G <u>(F)</u> P N/A UR	<u>RUBBER PADS</u>				
Corrosion Protection	E G <u>(F)</u> P N/A UR					
Span 1 of <u>1</u> (spans are numbered consecutively starting from the left abutment)						
Use "Additional Spans" Sheet for Multiple Spans						
DECK						
Item	Present Condition (circle)	Comments (a comment is mandatory if condition "Poor" is selected)				
Running Surface (N/A if running surface is gravel or timber planks)	E G F P <u>(N/A)</u> UR					
Running Planks	E <u>(G)</u> F P N/A UR	<u>MINOR TRACK DAMAGE 3" x 10</u>				
Sub-deck	E <u>(G)</u> F P N/A UR	<u>TREATED TIMBER 4" THICK</u>				
Ties	E G <u>(F)</u> P N/A UR	<u>TIMBER TREATED 200mm x 250mm</u>				
Nails	E <u>(G)</u> F P N/A UR					
Deck to Girder Bolts	E G F P <u>(N/A)</u> UR					
Concrete Deck	E G F P <u>(N/A)</u> UR					
Grout Pockets	E G F P <u>(N/A)</u> UR					
Deck Joints	E G F P <u>(N/A)</u> UR					
Steel Deck Plate	E G F P <u>(N/A)</u> UR					
Gravel Surface	E G F P <u>(N/A)</u> UR					
Gravel Deck Depth	metres or N/A					
Curb Rail/Blocks/Posts	E <u>(G)</u> F P UR	<u>TIMBER</u>				
Handrails/Walkouts	E G F P <u>(N/A)</u> UR					
Hardware	E <u>(G)</u> F P N/A UR					
Overall Deck Condition	E <u>(G)</u> F P UR					



**Routine Condition Bridge Inspection Form**
(except for log stringer or timber stringer bridges)

GENERAL INFORMATION			
*Site #: CK-2214		*Structure #:	
SUPERSTRUCTURE			
Item	Present Condition (circle)	Comments (a comment is mandatory if condition "Poor" is selected)	
Girders	E G <u>P</u> P UR	2X STEEL I-BEAMS	
Diaphragms	E G <u>F</u> P <u>N/A</u> UR		
Bracing	E G <u>P</u> P <u>N/A</u> UR		
Under-trussing	E G <u>F</u> P <u>N/A</u> UR		
Hardware	E G <u>F</u> P <u>N/A</u> UR		
Welded / Grouted Shear Connectors	E G <u>F</u> P <u>N/A</u> UR		
Stream CHANNEL			
*Est. Present Water Level Depth 0.5 (m)		*Est. Present Water Level Depth 0.0 (m)	*Est. Present Water Level Depth 0.8 (m)
HAZARDS (circle yes or no for each item)			
High Water?	Yes <u>No</u>	Scour?	Yes <u>No</u>
Ice?	Yes <u>No</u>	Debris?	Yes <u>No</u>
Aggradation?	Yes <u>No</u>		
Comments			
REPAIRS: ☐ Recommended ☐ Not required (H = High, M = Medium, L = Low)			
Repair Item #	*Priority (circle)	*Estimate (\$)	*Repair Description
1	H M L		
2	H M L		
3	H M L		
*Monitoring Status: ☐ Recommended ☐ Not required			
Monitor Item #	*Monitor Description		
1			
2			
PHOTO LOG			
Photo #	Description	Photo #	Description
	RIGHT TO LEFT		LEFT ABOUT X2
	LEFT TO RIGHT		FROM DOWNSTREAM.
	FROM UPSTREAM Y2		DOWNSTREAM
	RIGHT ABOUT		
INSPECTOR TO COMPLETE THIS SECTION			
As-built Drawings Checked? Yes <u>No</u>		P Eng Inspection Required? Yes <u>No</u>	
		Inspector's Estimate of Full Log Haul Traffic Replacement Date (year): (P Eng to review and evaluate Inspector's estimate, and to update "Full Log Haul Traffic Replacement (year)" on structure details screen in CBR)	
*Date of Inspection (yyyy/mm/dd) 2010-08-16	*Inspection Company Name Onsite Engineering Ltd	*Inspector's Name (print) Ali Sadeghi	Inspector's Signature
Inspector's Comments			
PROFESSIONAL ENGINEER (PEng) TO COMPLETE THIS SECTION			
Current Load Rating GWT (tonnes): (PEng to update structure details screen in CBR as necessary)		Date of Next Planned Inspection (yyyy/mm/dd)	
54		2012/09/02	
Reviewer Company Name MNRO	Reviewed by - PEng's Name (print) G. Dohm	Reviewed by - PEng's Sig 	Date Reviewed (yyyy/mm/dd) 2010/12/02
PEng Reviewer's Comments			


* Denotes Mandatory Information for Corporate Bridge Register



CK2214 Underneath




CK2214 Left abutment 2

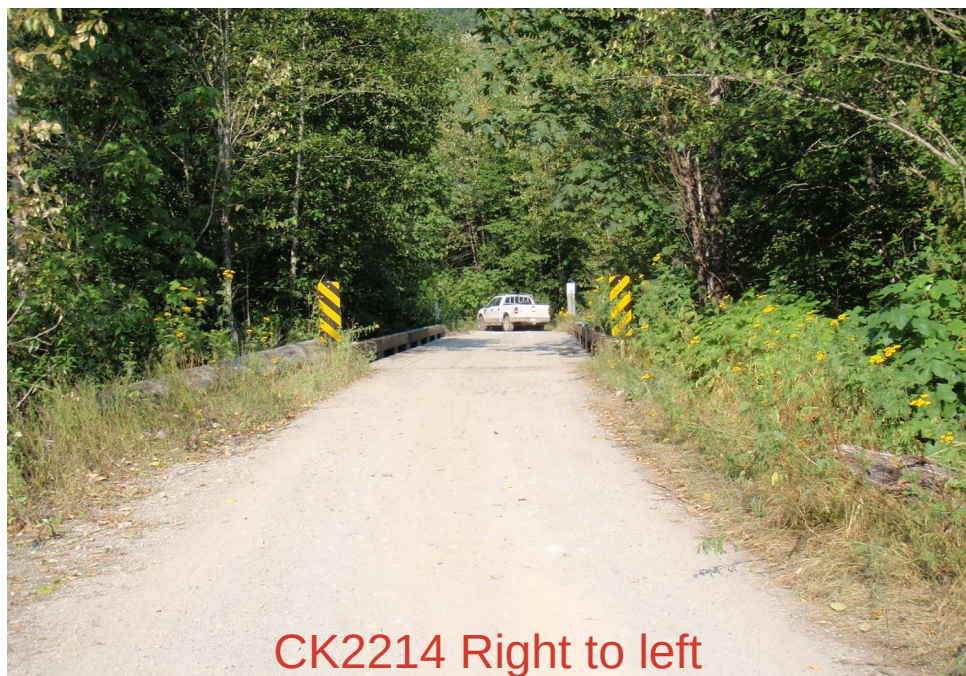

CK2214 Right to left



CK2214 From downstream

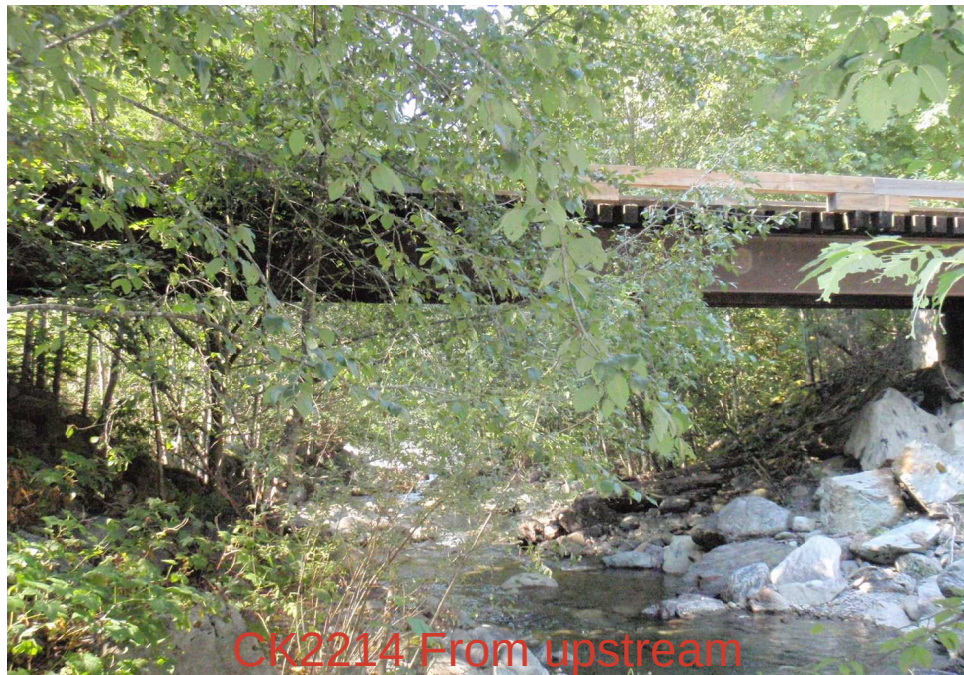

CK2214 From upstream



CK2214 Right abutment



CK2214 Left to right



CK2214 Left abutment
