

ACTIVE

Sept

BC Ministry of
Forests and Range

Page 1 of 2

Corporate Bridge Register (CBR) Structure Inventory Data Form "BRIDGES"

H12

GENERAL	
*Structure #	*Site #: CK2298
*Type/Class: ☒ Permanent Bridge ☐ Temporary Bridge	Crossing Name:
*Forest District: Chilliwack	Management Area:
*Forest Service Road: UETILUS CRK	Kilometres: 27.5
*Project File ID#: 7972	*Br. 01
Built For: ☐ BC Timber Sales ☐ Operations Division ☐ Other Commercial Users ☐ Road Permit Holder ☐ Road Use Permit Holder	
*Source: ☐ Inherited: Found Structure ☐ Inherited: From Oil & Gas/ ☐ Inherited: Non-Status Road Other Ministry ☐ Inherited: Reallocation ☐ Inherited: Transfers from ☐ New Structure Other Ministries ☐ Replacement Structure	
Year Built:	Year Added to Inventory:
Current Load Rating GVW (tonnes): (PEng to enter / update this value on structure details screen in CBR)	Design Load Rating GVW (tonnes): (Typically obtained from design drawings)
Design Vehicle Configuration: ☐ BCL625 ☐ CL625 ☐ L100 ☐ L120 ☐ L150 ☐ L165 ☐ L45 ☐ L60 ☒ L75 ☐ L90 ☐ Other	
*Primary User Client Number:	*Client Location Code:
Primary User Name:	
As Built Information on File? ☐ Yes ☐ No	
Installation Cost (\$):	Material Cost (\$):
REPLACEMENT DETAILS	
Original Replacement (year):	Estimated Closure (year):
Light Vehicle Traffic Replacement (year):	*Full Log Haul Traffic Replacement (year): (PEng to review and evaluate Inspector's estimate, and to enter /update this value on structure details screen in CBR).
Estimated Replacement Cost (\$):	
Replacement Cost Comments:	

* Denotes Mandatory Information for Corporate Bridge Register



BC Ministry of
Forests and Range

Page 2 of 2

Corporate Bridge Register (CBR)
Structure Inventory Data Form "BRIDGES"

STRUCTURAL DETAILS

Number of Spans: 1	Length of Spans (m) [e.g. for a 3-span bridge – 20, 35, 20] 17.2	
Number of Piers: —	Pier Type: ☐ Concrete ☐ Crib - Timber ☐ Piles - Concrete ☐ Piles - Steel ☐ Piles - Timber Treated ☐ Piles - Timber Untreated ☐ Steel Column on Concrete Pad	
Needle Beams? ☐ Yes ☒ No	Portable Structure? ☐ Yes ☒ No	Portable Superstructure Status: ☐ Installed ☐ Storage

Portable Superstructure Storage Location:

*Bridge Length (metres): 18.2m 60'	*Superstructure: ☐ Compo Girders ☐ Concrete Box Beam ☐ Rail Car ☐ Concrete Cast in Place ☐ Concrete I/T Beam ☐ Other ☐ Concrete Slab Girders ☐ Glulam Girder ☐ Log Stringer ☐ Steel Box Beam ☒ Steel I-Beam ☐ Steel Truss/Bailey/Acrow ☐ Timber-Treated Stringers ☐ Timber-Untreated Stringers		
--	---	--	--

*Deck Type: ☐ Concrete ☒ Concrete Composite ☐ Gravel ☐ Concrete Removable ☐ Concrete - Steel Free ☐ Steel ☐ Timber-Treated ☐ Timber-Untreated ☐ Other ☐ Timber-Treated Panels ☐ Timber-Untreated Panels	*Deck Width (metres): 4.9
---	------------------------------

*Running Surface: ☐ Anti-Skid ☐ Asphalt ☒ Concrete ☐ Gravel ☐ Not Available ☐ Timber Planks
--

*Left Abutment: ☐ Binwall ☐ Concrete Cast in Place ☐ Concrete Lock Blocks ☐ Concrete Precast ☐ Crib, Log or Untreated Timber ☐ Other ☐ Pile-Temporary Materials ☐ Pile-Permanent Materials ☐ Sill-Permanent Materials ☐ Sill-Temporary Materials ☒ Steel Pipe & Precast Pad	*Right Abutment: ☐ Binwall ☐ Concrete Cast in Place ☐ Concrete Lock Blocks ☐ Concrete Precast ☐ Crib, Log or Untreated Timber ☐ Other ☐ Pile-Temporary Materials ☐ Pile-Permanent Materials ☐ Sill-Permanent Materials ☐ Sill-Temporary Materials ☒ Steel Pipe & Precast Pad
--	---

Comments:

**Routine Condition Bridge Inspection Form**
(except for log stringer or timber stringer bridges)

GENERAL INFORMATION		(enter either long/lat or UTM below – not both)			
*Site #: <u>CK-2298</u>	*Crossing Name:	*Type/Class: ☐ Temporary bridge ☒ Permanent bridge	*Project File ID# <u>7992</u>		
*Structure #:			*Br. <u>01</u>		
*FSR Name: <u>UETILUS</u>	*Forest District: <u>Chilliwack</u>	*Kilometres: <u>27.5</u>	User km:		
Longitude: (ddd / mm / ss.s) <u>49 51 04.2</u>	☒ OR ☐ UTM	UTM Easting	UTM Northing		
Latitude: (ddd / mm / ss.s) <u>121 16 10.5</u>					
LEFT/RIGHT APPROACHES (as seen facing downstream) E = excellent; G = good; F = fair; P = poor; N/A = not appl., UR = Unrated					
Item	Present Condition (circle or fill-in)	Comments (a comment is mandatory if condition "Poor" is selected)			
Alignment	E G <u>(F)</u> P UR	Poor VISIBILITY DUE TO HOR CURVES.			
Bridge Ahead Signs Missing	<u>(0)</u> 1 2				
Brushing Required	<u>Yes</u> No				
Delineator Missing Left	<u>(0)</u> 1 2				
Delineator Missing Right	<u>(0)</u> 1 2				
Fender Condition	E G <u>(F)</u> P None UR	LOUIS			
Posted Load Rating	(tonnes) or <u>None</u>	NOT POSTED			
Road Surface	E G <u>(F)</u> P UR				
LEFT/RIGHT ABUTMENTS (as seen facing downstream)					
Item	Present Condition (circle)	Comments (a comment is mandatory if condition "Poor" is selected)			
Log/Timber Crib	E G F P <u>(N/A)</u> UR				
Tie-backs	E G F P <u>(N/A)</u> UR				
Bin Wall	E G F P <u>(N/A)</u> UR				
Concrete (cast in place; lock blocks, precast)	E G F P <u>(N/A)</u> UR				
Caps or Sills	E G F P <u>(N/A)</u> UR				
Piles or Posts	E <u>(G)</u> F P N/A UR	PIPE PILES.			
Ballast Wall	E <u>(G)</u> F P N/A UR	PRECAST CONCRETE			
Wing Wall	E G F P <u>(N/A)</u> UR				
Bracing	E <u>(G)</u> F P N/A UR	NOT VIS.			
Hardware	E <u>(G)</u> F P N/A UR				
Fill	E <u>(G)</u> F P N/A UR				
Riprap	E <u>(G)</u> F P N/A UR	WELL SORTED			
Bearings	E <u>(G)</u> F P N/A UR	RUBBER PADS			
Corrosion Protection	E <u>(G)</u> F P N/A UR				
Span 1 of <u>1</u> (spans are numbered consecutively starting from the left abutment)					
Use "Additional Spans" Sheet for Multiple Spans					
DECK					
Item	Present Condition (circle)	Comments (a comment is mandatory if condition "Poor" is selected)			
Running Surface (N/A if running surface is gravel or timber planks)	E G <u>(F)</u> P N/A UR				
Running Planks	E G F P <u>(N/A)</u> UR				
Sub-deck	E G F P <u>(N/A)</u> UR				
Ties	E G F P <u>(N/A)</u> UR				
Nails	E G F P <u>(N/A)</u> UR				
Deck to Girder Bolts	E G F P <u>(N/A)</u> UR				
Concrete Deck	E G <u>(F)</u> P N/A UR				
Grout Pockets	E G <u>(F)</u> P N/A UR				
Deck Joints	E G <u>(F)</u> P N/A UR				
Steel Deck Plate	E G F P <u>(N/A)</u> UR				
Gravel Surface	E G F P <u>(N/A)</u> UR				
Gravel Deck Depth	metres or <u>N/A</u>	1			
Curb Rail/Blocks/Posts	E G <u>(F)</u> B UR	UPSTREAM LEFT ABUT. RAIL DAMAGED. SOME LOOSE			
Handrails/Walkouts	E G F P <u>(N/A)</u> UR				
Hardware	E G <u>(F)</u> P N/A UR				
Overall Deck Condition	E G <u>(F)</u> P UR				

**Routine Condition Bridge Inspection Form**
(except for log stringer or timber stringer bridges)

GENERAL INFORMATION			
*Site #: CK-2298		*Structure #:	
SUPERSTRUCTURE			
Item	Present Condition (circle)	Comments (a comment is mandatory if condition "Poor" is selected)	
Girders	E <u>G</u> F P UR	2X STEEL I-BEAM L-75	
Diaphragms	E G F P <u>N/A</u> UR		
Bracing	E <u>G</u> F P N/A UR		
Under-trussing	E G F P <u>N/A</u> UR		
Hardware	E <u>G</u> F P N/A UR		
Welded / Grouted Shear Connectors	E G F P <u>N/A</u> UR		
Stream CHANNEL			
*Est. Present Water Level Depth 0.5 (m)		*Est. Present Water Level Depth with 12 (m)	*Est. Present Water Level Depth 1.3 (m)
HAZARDS (circle yes or no for each item)			
High Water?	Yes No <u>No</u>	Scour?	Yes No <u>No</u>
Ice?	Yes No <u>No</u>	Debris?	Yes No <u>No</u>
Aggradation?	Yes No <u>No</u>		
Comments			
REPAIRS: ☐ Recommended ☐ Not required (H = High, M = Medium, L = Low)			
Repair Item #	*Priority (circle)	*Estimate (\$)	*Repair Description
1	<u>H</u> M L		REPLACE DAMAGED SKIL -
2	<u>H</u> M L		
3	H M L		
*Monitoring Status: ☐ Recommended ☐ Not required			
Monitor Item #	*Monitor Description		
1			
2			
PHOTO LOG			
Photo #	Description	Photo #	Description
	RIGHT TO LEFT		RIGHT ABUT
	LEFT TO RIGHT		LEFT ABUT
	UPSTREAM		BRIDGE ID
	DOWNSTREAM		FROM UNDERNEATH
INSPECTOR TO COMPLETE THIS SECTION			
As-built Drawings checked? Yes No <u>No</u>		P Eng Inspection Required? Yes No <u>No</u>	
		Inspector's Estimate of Full Log Haul Traffic Replacement Date (year): (P Eng to review and evaluate Inspector's estimate, and to update "Full Log Haul Traffic Replacement (year)" on structure details screen in CBR)	
*Date of Inspection (yyyy/mm/dd) 2010-09-01	*Inspection Company Name Onsite Engineering Ltd	*Inspector's Name (print) Ali Sadeghi	Inspector's Signature
Inspector's Comments			
PROFESSIONAL ENGINEER (P Eng) TO COMPLETE THIS SECTION			
Current Load Rating GVW (tonnes): (P Eng to update structure details screen in CBR as necessary)		Date of Next Planned Inspection (yyyy/mm/dd)	
68		2013/09/01	
Reviewed by - P Eng's Name (print) On MNRO Engineering LTD	Reviewed by - P Eng's Name (print) G. Dohm	Reviewed by - P Eng's SI 	Date Reviewed (yyyy/mm/dd) 2010/12/08
P Eng Reviewer's Comments			

* Denotes Mandatory Information for Corporate Bridge Register



CK2298 Right to left



CK2298 Left to right



CK2298 From upstream




CK2298 From downstream



CK2298 Right abutment



CK2298 Left abutment

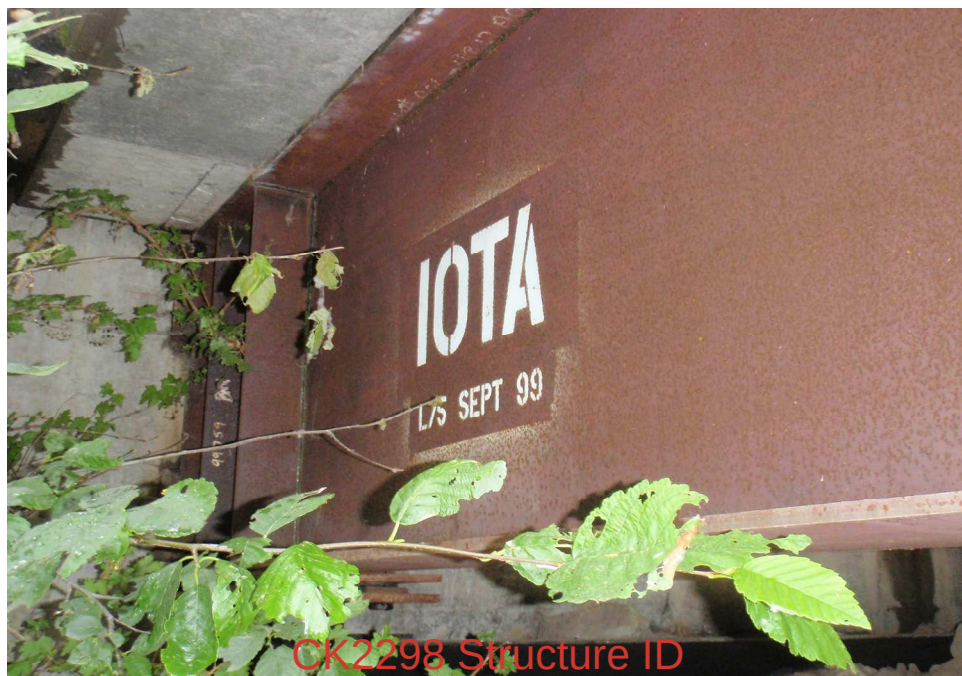

CK2298 Structure ID



CK2298 Underneath
