

CK-2190

LOST-BLACKLOCK 2.2km

2016 Inspection

CBR iPad Offline Ver 0.23



CBR Data

Latitude	Longitude
49°24'18.39"	-122°12'22.7"
Crossing Name	Side Creek
FSR #	8466
Branch #	11
Road Name	LOST-BLACKLOCK
User km	2.2
Current Load Rating (tonnes)	68
Structure Class	Permanent Bridge
Portable	N
Superstructure	Concrete Slab Girders
Deck Type	Concrete
Abutment Left	Steel Pipe and Precast Pad
Abutment Right	Steel Pipe and Precast Pad
Spans	1
Total Length (m)	9.2
Deck Width (m)	4.3

Updated Data

Latitude	Longitude
49°24'18.07"	-122°12'23.21"
HD Diff. (m)	14.3
Accuracy (m)	5

Inspection

Date of Inspection 2016-08-31 12:32:34 PM

Inspector Name Tyson Miller

Inspection Company MFLNRO

Inspector Comments

P.Eng Comments

Replace the guardrail, risers and blocks. Post bridge ahead signs and replace missing delineators. Brush approaches. Present load rating of L75 or 68 tonnes to



17/02/2017

P.Eng Seal

CK-2190

LOST-BLACKLOCK 2.2km

2016 Inspection



CBR iPad Offline Ver 0.23

Approach

Alignment Good

 Bridge Ahead Signs
Missing ☐ 0 ☐ 1 ☒ 2

Brushing Required Y

 Delineator Missing
Left ☐ 0 ☐ 1 ☒ 2

 Delineator Missing
Right ☐ 0 ☐ 1 ☒ 2

Fender Condition Good

Posted Load Rating not posted

Road Surface Fair

Abutment

Log/Timber Cribs N/A

Tie Backs N/A

Bin Wall N/A

Concrete N/A

Caps or Sills Good integrated ca/wall combo

Piles or Posts Unrated buried

Ballast Wall Good

Wing Wall N/A

Bracing Unrated buried

Hardware Poor loose rail bolts

Fill Good

Riprap Fair

Bearings Good

Corrosion Protection Unrated buried pipe columns

CK-2190

LOST-BLACKLOCK 2.2km

2016 Inspection

CBR iPad Offline Ver 0.23

**Deck**

Running Surface	Good	
Running Planks	N/A	
Sub Deck	N/A	
Ties	N/A	
Nails	N/A	
Deck to Girder Bolts	N/A	
Concrete Deck	N/A	
Grout Pockets	N/A	
Deck Joints	N/A	
Steel Deck Plate	N/A	
Gravel Surface	N/A	
Curb Rail/Blocks/Posts	Poor	rotten
Hand Rails/Walkouts	N/A	
Hardware	N/A	
Overall Deck Condition	Poor	due to rail condition
Gravel Depth (mm)		

CK-2190

LOST-BLACKLOCK 2.2km

2016 Inspection



CBR iPad Offline Ver 0.23

Steel/Concrete

Serial/ID Plate

Girders Good 3 concrete labs

Diaphragms N/A

Bracing N/A

Under Trussing N/A

Hardware N/A

Welded/grouted shear connectors Good welded

Log

Log Curbs

Needle Beam

Needle Lashing/
Shimming

Needle Beam to Crib (m)		Needle Diameter (mm)				
Stringer Number	Species	Peeled	Diameter (mm)	Rot Depth (mm)	Condition	Comment

CK-2190

LOST-BLACKLOCK 2.2km

2016 Inspection

CBR iPad Offline Ver 0.23



Hazards

Estimated Present Water Level Depth (m)	0.1	High Water	☐	Debris	☐
Estimated Present Water Level Width (m)	1.0	Aggradation	☐	Scour	☐
Estimated High Water Level Clearance (m)	2.0	Ice	☐		

Comments

Repairs and Monitoring

Repair Item	Priority	Repair Description
1	Medium	replace rail system prior to activity
2	Medium	brush approaches
3	Medium	post bridge ahead signs and replace missing delineators

Item	Monitor Description	Frequency
1		
2		
3		

Sketch
(Select Signature)




Approach from Right Bank when facing downstream



looking upstream



Deck

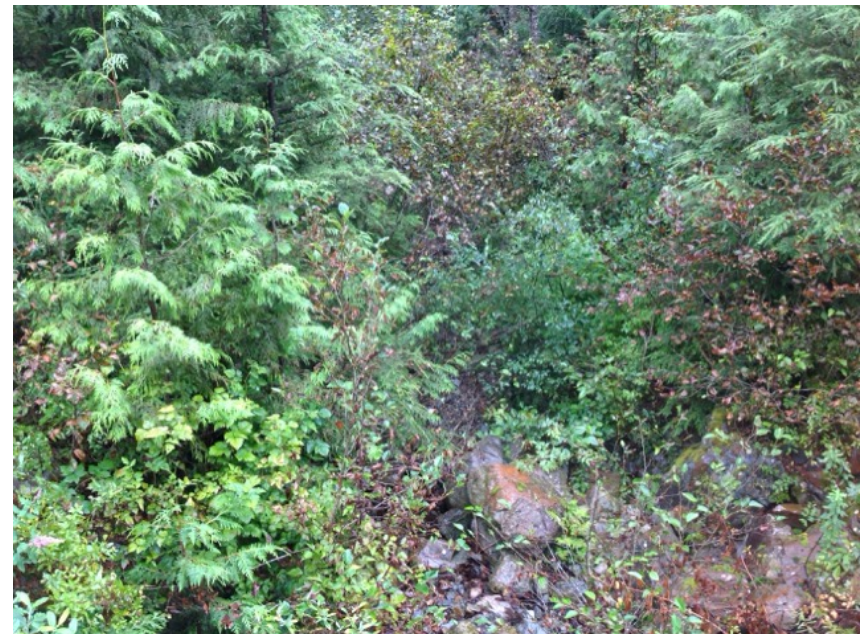

looking downstream



Approach from Left Bank when facing downstream



Left Bank Abutment when facing downstream



Right Bank Abutment when facing downstream
