

SC-8205
SC-8205

THEODOSIA 2.5km

2022 Inspection

CBR iPad Offline Ver 0.36



CBR Data

Latitude 49°58'52.29" Longitude -124°39'20.1"

Site Status Active

Insp. Status Inspect

Crossing Name Not Known

FSR # 6423 Branch # 7

Road Name THEODOSIA

User km 2.5

Previous Load Rating (tonnes) 150

Structure Class Permanent Bridge

Portable N

Superstructure Steel I-beam

Deck Type Concrete

Abutment Left Steel Pipe and Precast Pad

Abutment Right Steel Pipe and Precast Pad

Spans 1

Total Length (m) 12.2

Deck Width (m) 4.9

Updated Data

Latitude °0'0" Longitude °0'0"

HD Diff. (m) 5563881.1 Accuracy (m)

Inspection

Date of Inspection 2022-11-07 2:04:59 PM

Inspector Name Richard Mills

Inspector Comments Serial/ID Plate

Recommended Next Inspection 2025

Inspection Company MoF

P.Eng Comments

Load Rated by: Richard Mills, P.Eng. Jan 18, 2023

Load Rating: L165 or 150 tonnes

Next Inspection: 2025



PERMIT TO PRACTICE: 1003022

SC-8205
SC-8205

THEODOSIA 2.5km

2022 Inspection

CBR iPad Offline Ver 0.36



Approach

Alignment Good

Bridge Ahead Signs
Missing ☒ 0 ☐ 1 ☐ 2

Brushing Required N

Delineator Missing
Left ☒ 0 ☐ 1 ☐ 2

Delineator Missing
Right ☐ 0 ☒ 1 ☐ 2

Fender Condition Good

Posted Load Rating

Road Surface Good

Abutment

Log/Timber Cribs

Tie Backs

Bin Wall

Pier

Concrete Good

Caps or Sills Good

Piles or Posts Good

Ballast Wall Good

Wing Wall

Bracing Good

Hardware Good

Fill Good

Riprap Good

Bearings Good

Corrosion Protection Good

SC-8205
SC-8205

THEODOSIA 2.5km

2022 Inspection

CBR iPad Offline Ver 0.36



Deck

Running Surface **Good**

Running Planks

Sub Deck

Ties

Nails

Deck to Girder Bolts **Good**

Concrete Deck **Good**

Grout Pockets

Deck Joints **Good**

Steel Deck Plate

Gravel Surface

Curb Rail/Blocks/Posts **Good**

Hand Rails/Walkouts

Hardware **Good**

Overall Deck Condition **Good**

Gravel Depth (mm)

Pier Deck

SC-8205
SC-8205

THEODOSIA 2.5km

2022 Inspection

CBR iPad Offline Ver 0.36



Steel/Concrete

Girders Good

Diaphragms Good

Bracing Good

Under Trussing

Hardware Good

Welded/grouted
shear connectors

Log

Log Curbs

Needle Beam

Needle Lashing/
Shimming

Needle Beam to Crib (m)

Needle Diameter (mm)

Stringer
Number

Species

Peeled

Diameter
(mm)

Rot Depth
(mm)

Condition

Comment

SC-8205
SC-8205

THEODOSIA 2.5km

2022 Inspection

CBR iPad Offline Ver 0.36



Hazards

Estimated Present Water Level Depth (m) 0.1

High Water ☐

Debris ☐

Estimated Present Water Level Width (m) 0.3

Aggradation ☐

Scour ☐

Estimated High Water Level Clearance 3.5

Ic ☐

Comments

Repairs and Monitoring

Repair Item Repair Description

1

2

3

4

5

6

7

Item

Monitor Description

Frequency

1

2

3

SC-8205
SC-8205

THEODOSIA 2.5km

2022 Inspection


CBR iPad Offline Ver 0.36



Approach from Left Bank when facing downstream



Approach from Right Bank when facing downstream

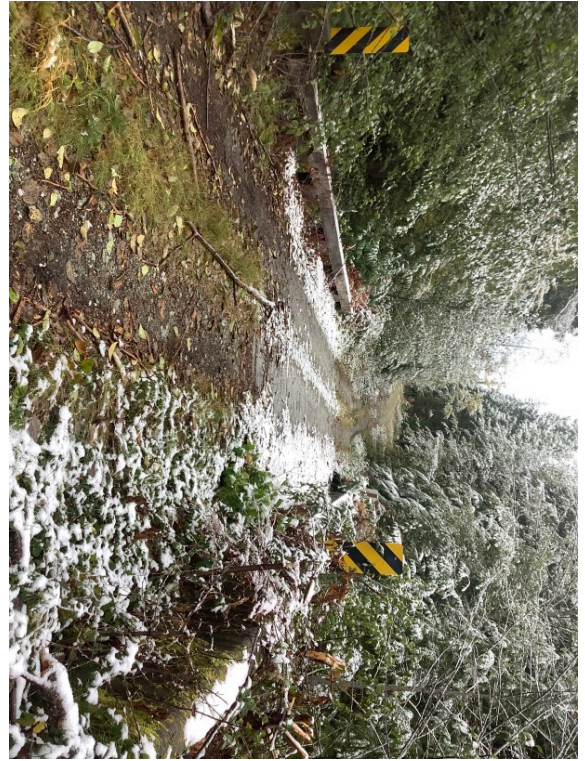

Upstream Profile



Deck



SC-8205
SC-8205

THEODOSIA 2.5km

2022 Inspection

CBR iPad Offline Ver 0.36



Left Bank Abutment when facing downstream

