

SQ-3033

LILLOOET WEST 01 70.2km

2019 Inspection



CBR iPad Offline Ver 0.31

CBR Data

Latitude	Longitude
49°48'15.09"	-122°13'26"
Crossing Name	Unknown
FSR #	8407
Branch #	1
Road Name	LILLOOET WEST 01
User km	70.2
Previous Load Rating (tonnes)	136
Structure Class	Permanent Bridge
Portable	N
Superstructure	Concrete Slab Girders
Deck Type	Concrete
Abutment Left	Steel Pipe and Precast Pad
Abutment Right	Steel Pipe and Precast Pad
Spans	1
Total Length (m)	10
Deck Width (m)	8

Updated Data

Latitude	Longitude
49°48'15.77"	-122°13'26.46"
HD Diff. (m)	22.8
Accuracy (m)	14

Inspection

Date of Inspection 2019-09-17 1:30:22 PM

Inspector Name Gino Fournier

Inspector Comments Serial/ID Plate

Recommended Next Inspection Year

Inspection Company FLNRORD

P.Eng Comments

Load Rated by: MFLNRORD, Greg Dohm, PEng., Jan. 24, 2020
Load Rating: L150 or 136 tonnes
Next Inspection: 2022
Comments:



P.Eng Seal

SQ-3033

LILLOOET WEST 01 70.2km

2019 Inspection



CBR iPad Offline Ver 0.31

Approach

Alignment Fair

Bridge Ahead Signs
Missing ☒ 0 ☐ 1 ☐ 2

Brushing Required N

Delineator Missing
Left ☒ 0 ☐ 1 ☐ 2Delineator Missing
Right ☒ 0 ☐ 1 ☐ 2

Fender Condition Good No posts all sides

Posted Load Rating 136

Road Surface Good

Abutment

Log/Timber Cribs N/A

Tie Backs N/A

Bin Wall N/A

Pier N/A

Concrete N/A

Caps or Sills Good

Piles or Posts Unrated Can't see them.

Ballast Wall Good

Wing Wall N/A

Bracing N/A

Hardware N/A

Fill Good

Riprap Good

Bearings Good

Corrosion Protection N/A

SQ-3033

LILLOOET WEST 01 70.2km

2019 Inspection

CBR iPad Offline Ver 0.31

**Deck**

Running Surface Good

Running Planks N/A

Sub Deck N/A

Ties N/A

Nails N/A

Deck to Girder Bolts N/A

Concrete Deck Good

Grout Pockets N/A

Deck Joints Good

Steel Deck Plate N/A

Gravel Surface N/A

Curb Rail/Blocks/Posts Good

Hand Rails/Walkouts N/A

Hardware N/A

Overall Deck Condition Good

Gravel Depth (mm)

Pier Deck

SQ-3033

LILLOOET WEST 01 70.2km

2019 Inspection



CBR iPad Offline Ver 0.31

Steel/Concrete

Girders Good

Diaphragms N/A

Bracing N/A

Under Trussing N/A

Hardware N/A

Welded/grouted
shear connectors Good**Log**

Log Curbs N/A

Needle Beam N/A

Needle Lashing/
Shimming

Needle Beam to Crib (m)

Needle Diameter (mm)

Stringer Number	Species	Peeled	Diameter (mm)	Rot Depth (mm)	Condition	Comment
--------------------	---------	--------	------------------	-------------------	-----------	---------

SQ-3033

LILLOOET WEST 01 70.2km

2019 Inspection

CBR iPad Offline Ver 0.31



Hazards

Estimated Present Water Level Depth (m)	0	High Water	☐	Debris	☐
Estimated Present Water Level Width (m)	0	Aggradation	☐	Scour	☐
Estimated High Water Level Clearance (m)	2.5	Ice	☐		

Comments

Repairs and Monitoring

Repair Item	Priority	Repair Description
-------------	----------	--------------------

1

2

3

Item	Monitor Description	Frequency
------	---------------------	-----------

1

2

3

Sketch
(Select Signature)



Approach from Left Bank when facing downstream



Downstream from Crossing



Approach from Right Bank when facing downstream



Upstream from Crossing




Downstream Profile



Right Bank Abutment when facing downstream



Left Bank Abutment when facing downstream

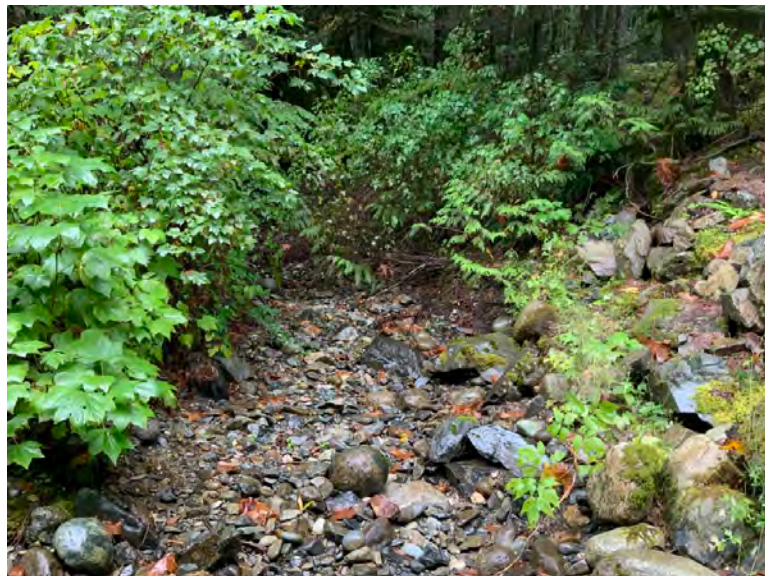

Upstream Profile



Structure ID
