

SQ-3051

LEVETTE LAKE 01 2.7km

2019 Inspection

CBR iPad Offline Ver 0.31



CBR Data

Latitude	Longitude
49°49'19.8"	-123°10'46.9"
Crossing Name	Evans Creek
FSR #	6425
Branch #	1
Road Name	LEVETTE LAKE 01
User km	2.7
Previous Load Rating (tonnes)	63
Structure Class	Permanent Bridge
Portable	N
Superstructure	Concrete Slab Girders
Deck Type	Concrete
Abutment Left	Steel Pipe and Precast Pad
Abutment Right	Steel Pipe and Precast Pad
Spans	1
Total Length (m)	9
Deck Width (m)	4.3

Updated Data

Latitude	Longitude
°0'0"	°0'0"
HD Diff. (m)	5546178.3
Accuracy (m)	

Inspection

Date of Inspection 2019-09-18 2:21:41 PM

Inspector Name Richard Mills


Inspector Comments Serial/ID Plate

Recommended Next Inspection Year

Inspection Company FLNRORD

P.Eng Comments

Load Rated by: MFLNRORD, Greg Dohm, PEng., January 29, 2020
Load Rating: BCL625 or 63 tonnes
Next Inspection: 2022
Comments:



P.Eng Seal

SQ-3051

LEVETTE LAKE 01 2.7km

2019 Inspection



CBR iPad Offline Ver 0.31

Approach

Alignment Fair

Bridge Ahead Signs
Missing ☒ 0 ☐ 1 ☐ 2

Brushing Required N

Delineator Missing
Left ☒ 0 ☐ 1 ☐ 2Delineator Missing
Right ☒ 0 ☐ 1 ☐ 2

Fender Condition Good

Posted Load Rating

Road Surface Good

Abutment

Log/Timber Cribs N/A

Tie Backs N/A

Bin Wall N/A

Pier N/A

Concrete Good

Caps or Sills Good

Piles or Posts Good

Ballast Wall Good

Wing Wall N/A

Bracing N/A

Hardware Good

Fill Good

Riprap Fair Erosion right side. Monitor.

Bearings Good

Corrosion Protection N/A

SQ-3051

LEVETTE LAKE 01 2.7km

2019 Inspection

CBR iPad Offline Ver 0.31

**Deck**

Running Surface Good

Running Planks N/A

Sub Deck N/A

Ties N/A

Nails N/A

Deck to Girder Bolts N/A

Concrete Deck Good

Grout Pockets N/A

Deck Joints Good

Steel Deck Plate N/A

Gravel Surface N/A

Curb Rail/Blocks/Posts Fair

Hand Rails/Walkouts N/A

Hardware Good

Overall Deck Condition Good

Gravel Depth (mm)

Pier Deck

SQ-3051

LEVETTE LAKE 01 2.7km

2019 Inspection

CBR iPad Offline Ver 0.31

**Steel/Concrete**

Girders Good

Diaphragms N/A

Bracing N/A

Under Trussing N/A

Hardware N/A

Welded/grouted
shear connectors Good**Log**

Log Curbs

Needle Beam

Needle Lashing/
Shimming

Needle Beam to Crib (m)

Needle Diameter (mm)

Stringer
Number

Species

Peeled

Diameter
(mm)Rot Depth
(mm)

Condition

Comment

SQ-3051

LEVETTE LAKE 01 2.7km

2019 Inspection

CBR iPad Offline Ver 0.31



Hazards

Estimated Present Water Level Depth (m)	0.2	High Water	☐	Debris	☐
Estimated Present Water Level Width (m)	2.0	Aggradation	☐	Scour	☒
Estimated High Water Level Clearance (m)	1.5	Ice	☐		

Comments

Repairs and Monitoring

Repair Item	Priority	Repair Description
-------------	----------	--------------------

1

2

3


Item	Monitor Description	Frequency
------	---------------------	-----------

1 Onitor scour right abutment

2

3

Sketch
(Select Signature)

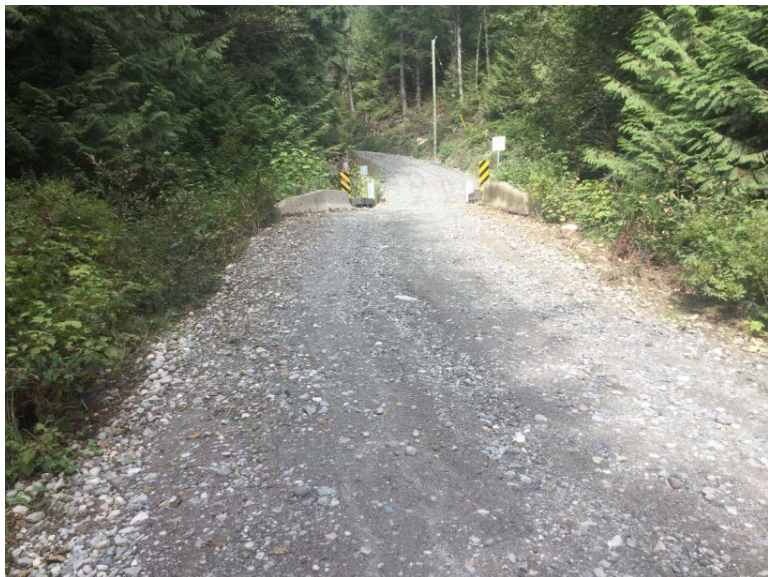

Approach from Right Bank when facing downstream



Deck



Approach from Left Bank when facing downstream



Right Bank Abutment when facing downstream



Left Bank Abutment when facing downstream
