

SQ-3066
SQ-3066

IN-SHUCK-CH FSR 55.8km

2021 Inspection

CBR iPad Offline Ver 0.33



CBR Data

Latitude	Longitude
49°55'38.79"	-122°20'25.6"
Crossing Name	Livingston Creek
FSR #	7343
Branch #	1
Road Name	IN-SHUCK-CH FSR
User km	55.8
Previous Load Rating (tonnes)	63
Structure Class	Permanent Bridge
Portable	N
Superstructure	Steel I-beam
Deck Type	Concrete Composite
Abutment Left	Steel Pipe and Precast Pad
Abutment Right	Steel Pipe and Precast Pad
Spans	1
Total Length (m)	27
Deck Width (m)	4.8

Updated Data

Latitude	Longitude
49°55'38.36"	-122°20'26.88"
HD Diff. (m)	29.0
Accuracy (m)	6

Inspection

Date of Inspection 2021-08-24 9:00:57 AM

Inspector Name Forrest Simpson

Inspector Comments Serial/ID Plate

Recommended Next Inspection Year

Inspection Company FLNRORD

P.Eng Comments

Load Rated by: MFLNRORD, Greg Dohm, PEng., Nov. 12, 2021
Load Rating: BCL625 or 63 tonnes
Next Inspection: 2024
Comments:



P.Eng Seal

SQ-3066
SQ-3066

IN-SHUCK-CH FSR 55.8km

2021 Inspection

CBR iPad Offline Ver 0.33



Approach

Alignment Good

Bridge Ahead Signs
Missing ☐ 0 ☒ 1 ☐ 2 Town approach

Brushing Required Y Minor brushing

Delineator Missing
Left ☒ 0 ☐ 1 ☐ 2

Delineator Missing
Right ☒ 0 ☐ 1 ☐ 2

Fender Condition Good

Posted Load Rating 62

Road Surface Good

Abutment

Log/Timber Cribs

Tie Backs

Bin Wall

Pier

Concrete Good

Caps or Sills

Piles or Posts Good

Ballast Wall Good

Wing Wall

Bracing Good

Hardware Good

Fill Good

Riprap Good

Bearings

Corrosion Protection Good

SQ-3066
SQ-3066

IN-SHUCK-CH FSR 55.8km

2021 Inspection

CBR iPad Offline Ver 0.33



Deck

Running Surface **Good**

Running Planks

Sub Deck

Ties

Nails

Deck to Girder Bolts

Concrete Deck **Good**

Grout Pockets **Unrated** Not visible

Deck Joints **Good**

Steel Deck Plate

Gravel Surface

Curb Rail/Blocks/Posts **Excellent** New hss

Hand Rails/Walkouts

Hardware **Good**

Overall Deck Condition **Good**

Gravel Depth (mm)

Pier Deck

SQ-3066
SQ-3066

IN-SHUCK-CH FSR 55.8km

2021 Inspection

CBR iPad Offline Ver 0.33



Steel/Concrete

Girders Good

Diaphragms Good

Bracing Good

Under Trussing

Hardware Good

Welded/grouted
shear connectors

Log

Log Curbs

Needle Beam

Needle Lashing/
Shimming

Needle Beam to Crib (m)

Needle Diameter (mm)

Stringer
Number

Species

Peeled

Diameter
(mm)

Rot Depth
(mm)

Condition

Comment

SQ-3066
SQ-3066

IN-SHUCK-CH FSR 55.8km

2021 Inspection

CBR iPad Offline Ver 0.33



Hazards

Estimated Present Water Level Depth (m)	.5	High Water	☐	Debris	☐
Estimated Present Water Level Width (m)	5	Aggradation	☐	Scour	☐
Estimated High Water Level Clearance (m)	4	Ice	☐		

Comments

Repairs and Monitoring

Repair Item	Repair Description
-------------	--------------------

1

2

3

4

5

6

7

Item

Monitor Description

Frequency

1

2

3



Approach from Left Bank when facing downstream



Deck



Left Bank Abutment when facing downstream



Right Bank Abutment when facing downstream



2021 Inspection

CBR iPad Offline Ver 0.33

IN-SHUCK-CH FSR 55.8km

SQ-3066
SQ-3066




Structure ID



Superstructure



Left Bank Abutment when facing downstream

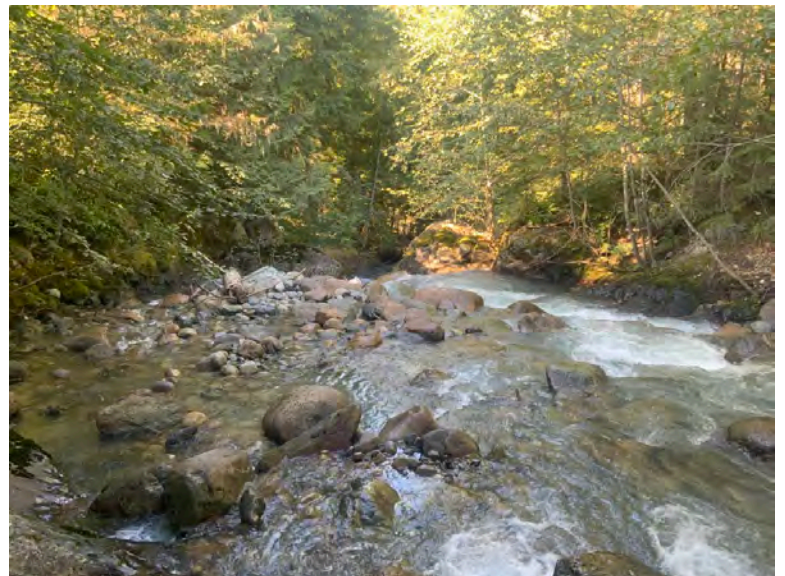

Downstream from Crossing



Upstream from Crossing



Approach from Right Bank when facing downstream



Right Bank Abutment when facing downstream
