Planting Map

BCTS
BC Timber Sales

TSL **A94168**	Block ID 2
Business Area Cariboo-Chilcotin	UBI BL5YB
Operating Area Cariboo	Management Unit Williams Lake
Gross Block Area 47.73	NAR 41.39
Min. Elev. 940 / Max. Elev. 960	Geographic Center **Latitude** 52 26 50 **Longitude** -121 10 52
Location Whiffle Lake	Opening 093A045-132

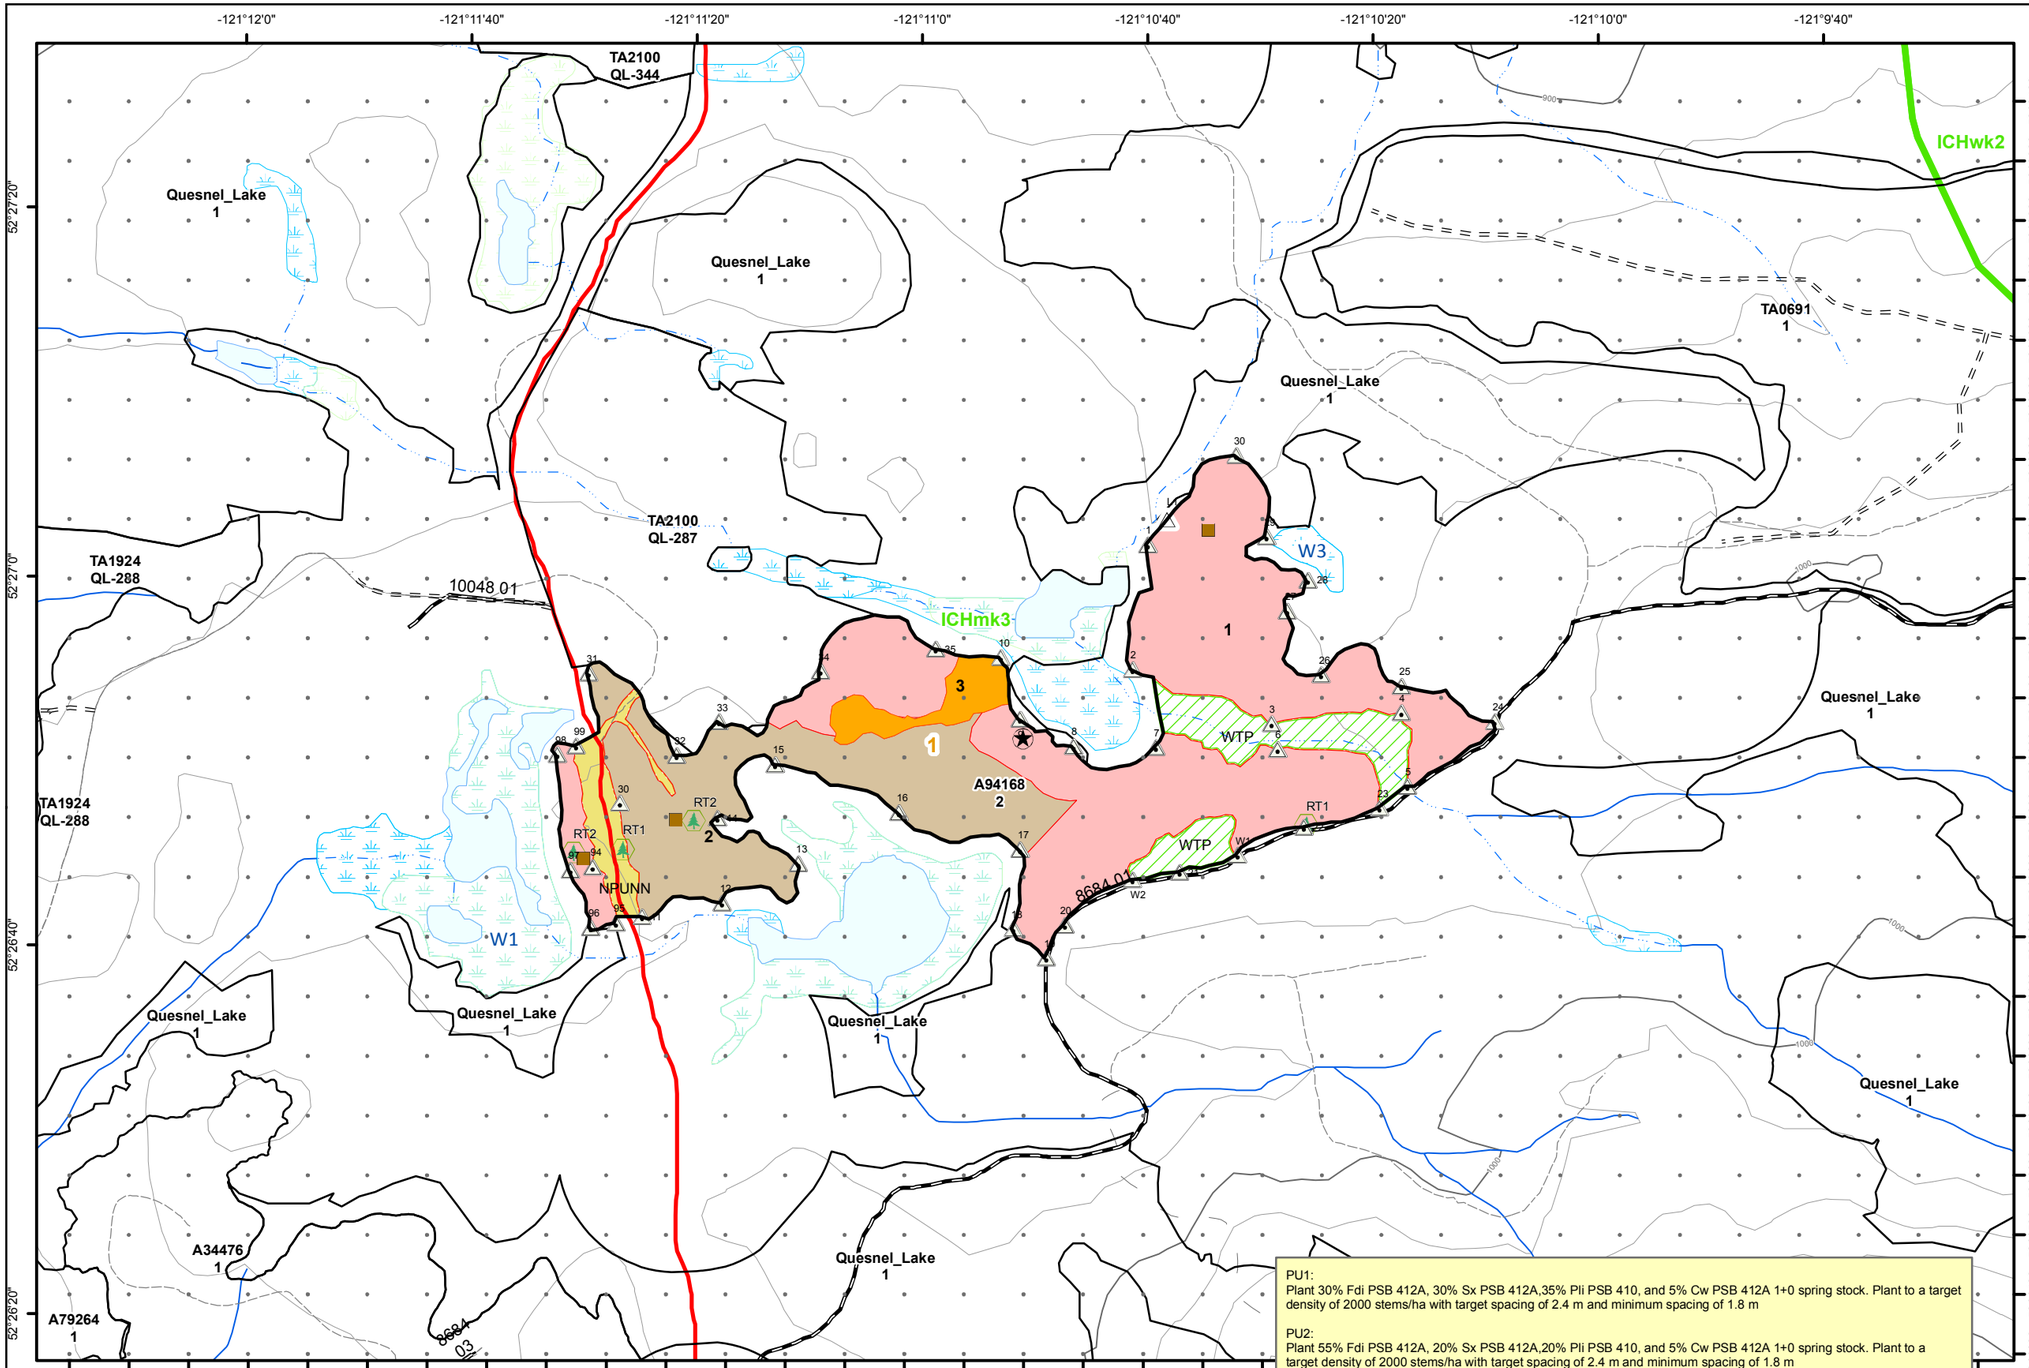

Planting Unit
1
2
3

BCTS All Blocks
Block of Interest
Ecology Unit
Biogeoclimatic Zone

BCTS GPS Stations
GPS Station
Block Bdy Hub
Falling Corners
Reference Trees

BCTS Layout Points
Ecology Plot
Block Centre
Woody Debris
Landing Cable
Landing Ground
R/W Landing
Slump/Slide Area
Rock Outcrops
Cross Ditch
Arch Pipe
Arch Pipe, Proposed
Culvert
Culvert, Proposed
Bridge
Bridge, Proposed
Bridge, Condemned
Removed Structures
Gate
Road Barrier
Cattle Guard
Pipeline Crossing
Cave/ Den
Mineral Lick
Nest
Wildlife Tree
Wildlife Feature

BCTS Line Features
Fence Line
Other Trail
Pipe Line
Rec Trail
Seismic Line
Cliff
Draw
Embankment
Gully
Ridge
Slope Break
Cultural/Heritage Feature

BCTS Streams Class
Unknown
INT;NCD
S1;S2;S3;S4
S5;S6

BCTS Roads - Road State
Deactivated Road
Existing Road
Proposed Road
Unknown/NULL
Rehab Road

TRIM Features
River or Stream - Definite
River or Stream - Indefinite
Contour - Index
Contour - Intermediate
Road Permit
Forest Service Road
Highway/Main/Paved Road
Gravel/Resource Road
Trail
Snow Shed (Railway)
Tunnel
Bridge
Airstrip
Rail Line
Pipeline / Wellsite

CLA
WTP
WTRA
NP Permanent Access
Reserve
NP Immature
Area of Concern
Slope Area (>35%)
SAR Cliff
SAR Forested
SAR Rare Ecosystems
Special Mgmt Area
Tailing Pond
Lake/Watercourse
Marsh
Swamp
Private Land
Protected Areas/ Parks

Riparian Features
MFZ / MSZ
RMZ
RRZ

Planting Unit	Area (ha)	Status	Density (/ha)	Spacing (m) Target	Min	Max	Trees / Unit	Species Composition Detail *
1	26.88	Planned	2000	2.4	1.8		54507	Cw-5-0+0-none-none-none-2725, Fdi-30-0+0-none-none-none-16352, Sx-30-0+0-none-none-none-16352, Pli-35-0+0-none-none-none-19078
2	12.74	Planned	2000	2.4	1.8		25725	Cw-5-0+0-none-none-none-1286, Pli-20-0+0-none-none-none-5145, Sx-20-0+0-none-none-none-5145, Fdi-55-0+0-none-none-none-14149
3	1.76	Planned	1400	2.9	1.8		1780	Cw-5-0+0-none-none-none-89, Pli-45-0+0-none-none-none-801, Sx-50-0+0-none-none-none-890
		Planned						

*(Species - Species % - Stock Age - Stock Type - Request Key - Seedlot - # Trees/Species)

Access Instructions

From Williams Lake travel south on Highway 97 14.2 km to the Horsefly Road. Turn left onto the Horsefly Road and travel to Horsefly. At Clarke's General Store turn right onto the Horsefly Lake Road and cross the Horsefly River. Travel 1.3 km and turn left onto the Z Road. Travel to 22.1 km on Z Road, turn right onto Viewland FSR. In 2.4 km is the POC of 8684.01-05, continue for 0.2 km to the POC of 8684.01-06.

PU1:
Plant 30% Fdi PSB 412A, 30% Sx PSB 412A,35% Pli PSB 410, and 5% Cw PSB 412A 1+0 spring stock. Plant to a target density of 2000 stems/ha with target spacing of 2.4 m and minimum spacing of 1.8 m

PU2:
Plant 55% Fdi PSB 412A, 20% Sx PSB 412A,20% Pli PSB 410, and 5% Cw PSB 412A 1+0 spring stock. Plant to a target density of 2000 stems/ha with target spacing of 2.4 m and minimum spacing of 1.8 m

PU 3:
Plant 50% Sx PSB 412A, 45% Pli PSB 410, and 5% Cw PSB 412A 1+0 spring stock. Plant to a target density of 1400 stems/ha with target spacing of 2.9 m and minimum spacing of 1.8 m

First priority: Plant on screefed areas and on mounds.
Second priority: Plant between screefs/mounds to meet target (within 10cm of stumps/ coarse woody debris-boot screef required 20cmx20cm). Use minimum spacing to ensure optimal microsites are utilized and to maintain target density.

Plant the rehabilitated roads- mix bag. Plant Fdi on sloped areas >10% and ridges. Plant 100 % pine within burnt piles. Ignore natural regeneration (if any). MS

0 100 200 300 400 500 Meters

1:10,000

N W E S

Date August 22, 2022 **User** MRHEES
Template Name BlockPlantingMap_NFiscal_11x17L_v3
Coordinate System NAD 1983 UTM Zone 10N
